

SECRET

25X1

13 August 1964

Dear John:

Subject: Contract [redacted]
PAR 215, Roller Transport Processor (24-Inch)

We are submitting herewith a new estimate for PAR 215 in accordance with agreements reached during the 8 - 11 June 1964 Quarterly Progress Review. The attached estimate was redone to reflect the following changes.

1. Delete requirement to process continuous web material, 20-inches wide.
2. Delete requirement for cassette feed.
3. Delete requirement for take-up module to handle continuous web materials, 20-inches wide up to 250 feet long.

Although the attached estimate shows only a small reduction in cost (see Column 3 Fiscal Summary, [redacted] Quarterly Report dated 1 June 1964), it now covers cost for installation and checkout of the processor at the customer's facility.

Also included are tentative schedules for design, fabrication, test and delivery of processors on both PARs 214 and 215.

RRW:jid
Enclosures

Dick
Dick

25X1


25X1

Approved For Release 2005/02/17 : CIA-RDP78B04770A001100050021-3

Approved For Release 2005/02/17 : CIA-RDP78B04770A001100050021-3

RT-24 Processor

PAR 215
7 Aug 64

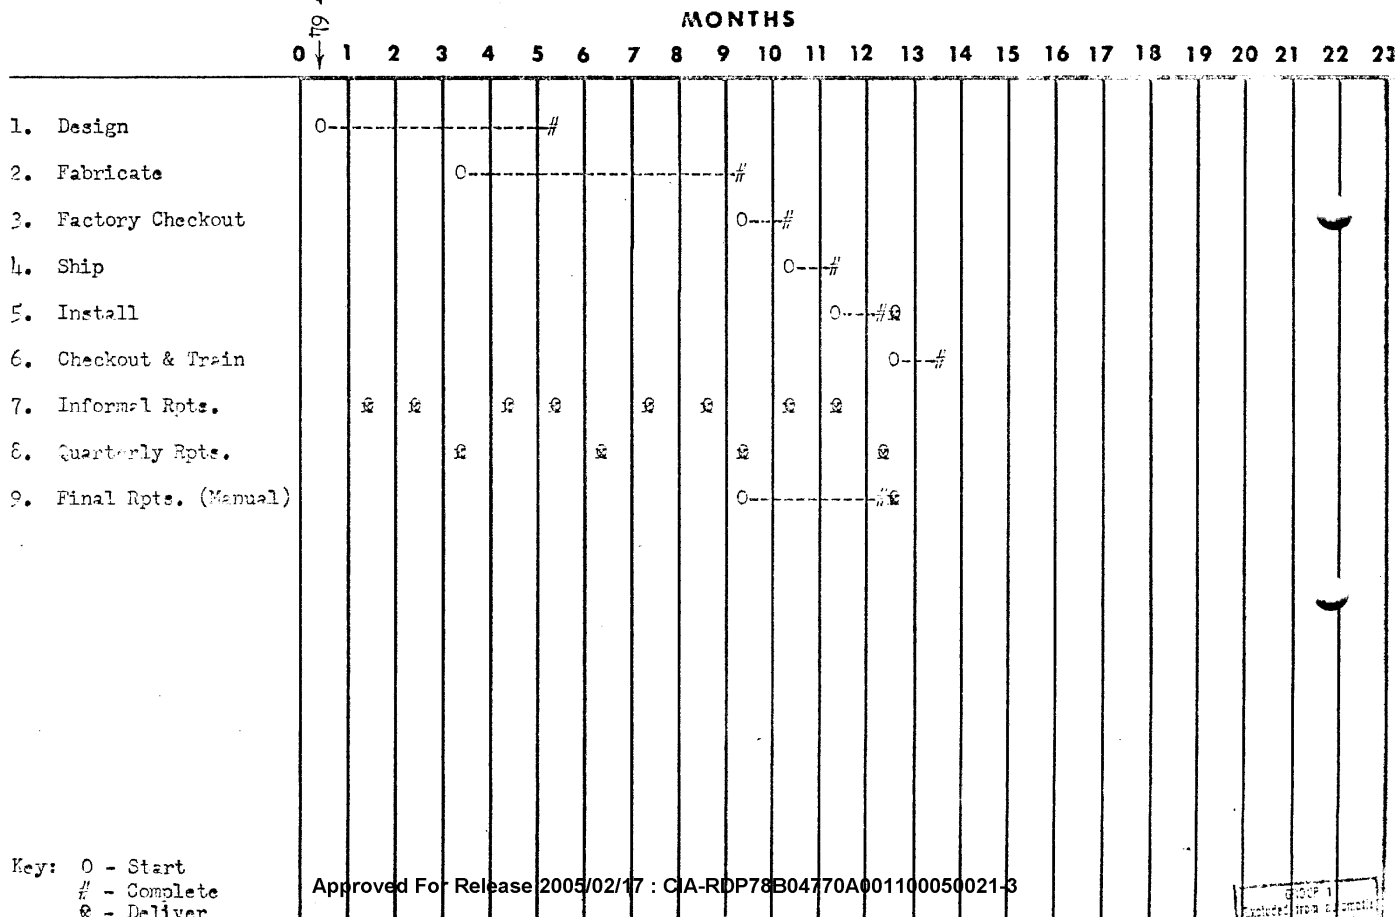

SECRET

25X1

25X1

SECRET 112135Z

SPX
8-18-64
12 Aug
file RPD
11 Sep 64

IN 8619

B. MINUTES QUARTERLY PROGRESS REVIEW CONTRACT

25X1

DATED 25 JUNE 64.

25X1

1.

2. PAR 215, ROLLER TRANSPORT PROCESSOR (24-INCH) HAS BEEN

ESTIMATED IN ACCORDANCE WITH CHANGES REQUESTED BY REF B AND

CITED IN PARAGRAPH 3 REF A. NEW ESTIMATE IS AS FOLLOWS:

- A. LABOR
- B. BURDEN AT 182 PERCENT
- C. TOTAL
- D. "SUBCONTRACT" (WITHIN BAIL)
- E. TRAVEL AND SUBSISTENCE
- F. FACTORY COST
- G. G & A AT 6.5 PERCENT
- H. TOTAL COST
- I. FEE
- J. TOTAL EST. OFFER PRICE

25X1

4

3. ALTHOUGH THE ABOVE ESTIMATE SHOWS ONLY A SMALL REDUCTION

25X1

IN COST (SEE COL. 3 FISCAL SUMMARY QUARTERLY REPORT

DATED 1 JUNE 64), IT NOW COVERS COST FOR INSTALLATION AND

25X1

CHECKOUT OF THE PROCESSOR AT KWS SITE.

4. COMPLETE ESTIMATE SUMMARY AND TENTATIVE PRODUCTION

SECRET

GROUP 1
 Excluded from automatic
 downgrading and
 declassification

25X1 SCHEDULE ARE BEING FORWARDED BY [REDACTED]

5. A TENTATIVE PRODUCTION SCHEDULE FOR PAR 214, FOLLOWS
TRANSPORT PROCESSOR (12-INCH) IS ALSO BEING FORWARDED.

6. SCHEDULES REF ABOVE DO ~~NOT~~ REPEAT ~~NOT~~ REFLECT CHANGES
THAT MAY BE POSSIBLE IN ACCORDANCE WITH [REDACTED] REQUEST
TO EXPEDITE PAR 215. ANY SUCH CHANGES THAT WILL EXPEDITE
DELIVERY OF PAR 215 WILL BE FORWARDED AFTER COMPLETE REVIEW
OF WORK LOADS AND PRODUCTION SCHEDULES.

SECRET

END OF MESSAGE
